




# Culver City Park Improvement Projects

Culver City Parks, Recreation & Community Services



August 2026





# **Culver City Park – Active Projects**

**Bill Botts Field Modifications  
Field Improvements #2, 3, 4**

**Slope Clearance & Goats  
Dog Park Improvements  
Fitness Court and Shade Structure  
Trail Feasibility Study  
Tree Survey**

# Bill Botts Field (#1)

This project will adjust the infield for youth baseball and softball.  
15,000 square feet of infield clay is being replaced with turf grass.

Status: PRCs staff has removed the infield clay and stockpiled for reuse at the upper ballfields.

Irrigation modifications are underway.

Topsoil will be ordered for installation in early August.

Turf grass will be ordered for installation in late August.

Field Opening: September 2026

# BILL BOTTS FIELD FIELD IMPROVEMENT PLAN


AUGUST 2025

## PROJECT SUMMARY

THIS PROJECT WILL RENOVATE THE EXISTING ADULT BASEBALL FIELD INTO A YOUTH FIELD BY REDUCING THE CLAY INFIELD, INSTALLING NEW GRASS AND IRRIGATION.

## IMPROVEMENT LEGEND

- 01 NEW OUTFIELD GRASS  
13,643 S.F. TOTAL
- 02 EXISTING CLAY INFIELD - 'ANGEL MIX'  
REDUCE SIZE TO YOUTH BASEBALL & SOFTBALL  
11,890 S.F. TOTAL
- 03 EXISTING OUTFIELD GRASS  
PROTECT-IN-PLACE
- 04 TEMPORARY OUTFIELD FENCE  
NOT IN PROJECT SCOPE
- 05 EXISTING FENCE  
NOT IN PROJECT SCOPE

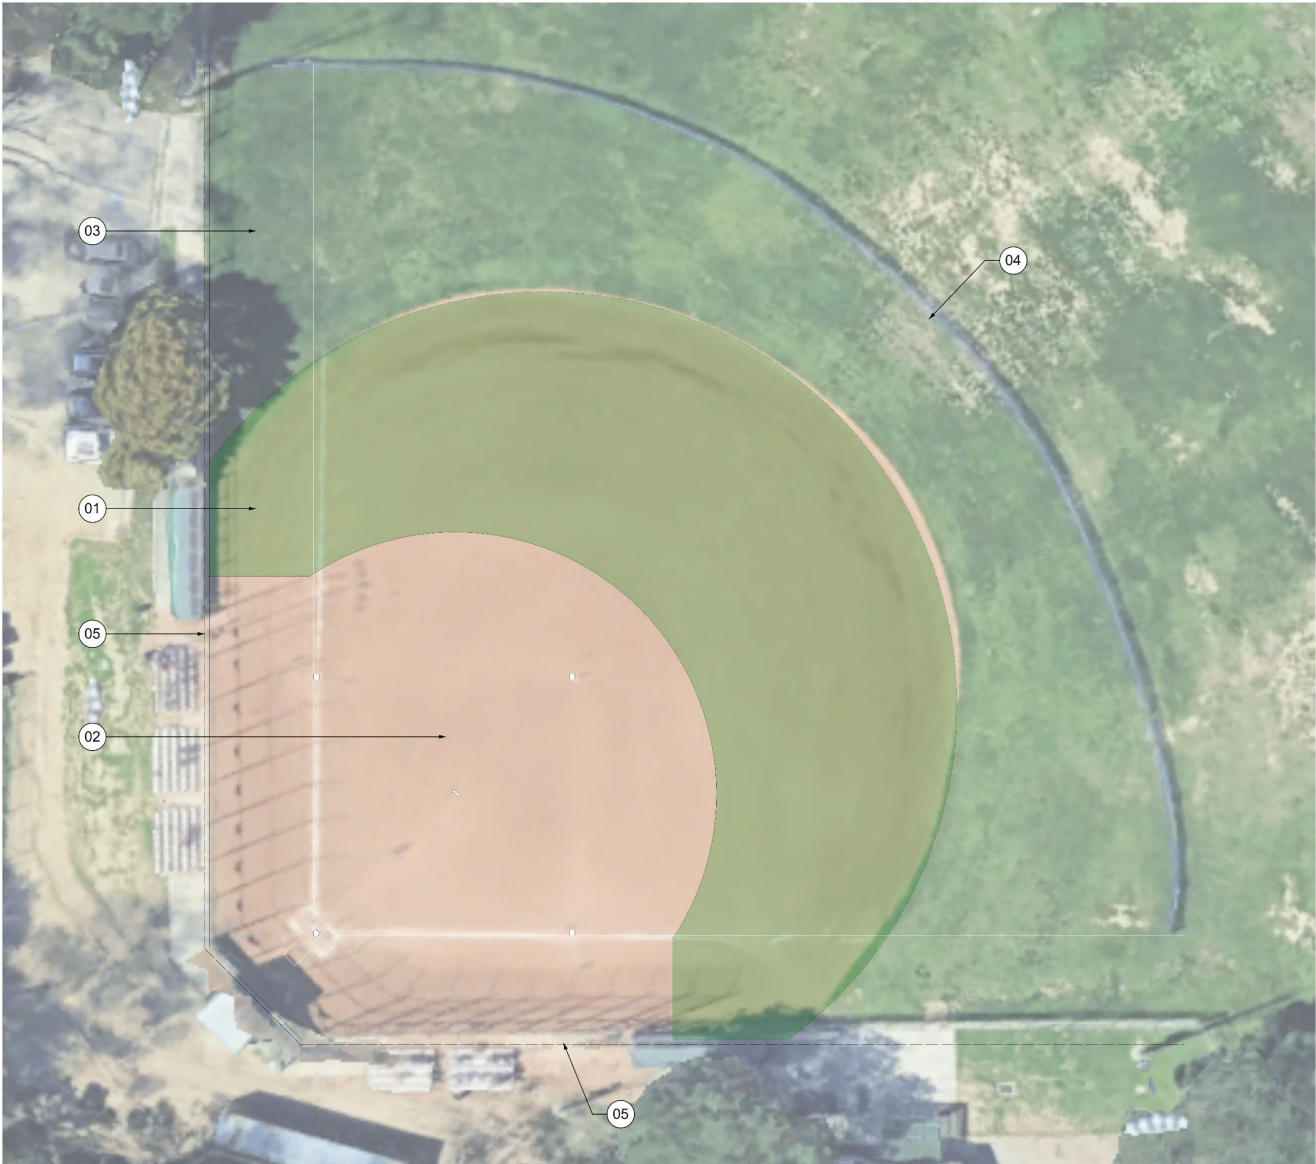


LANDSCAPE PLAN




*Culver* CITY



PRCS Crew at Bill Botts Field

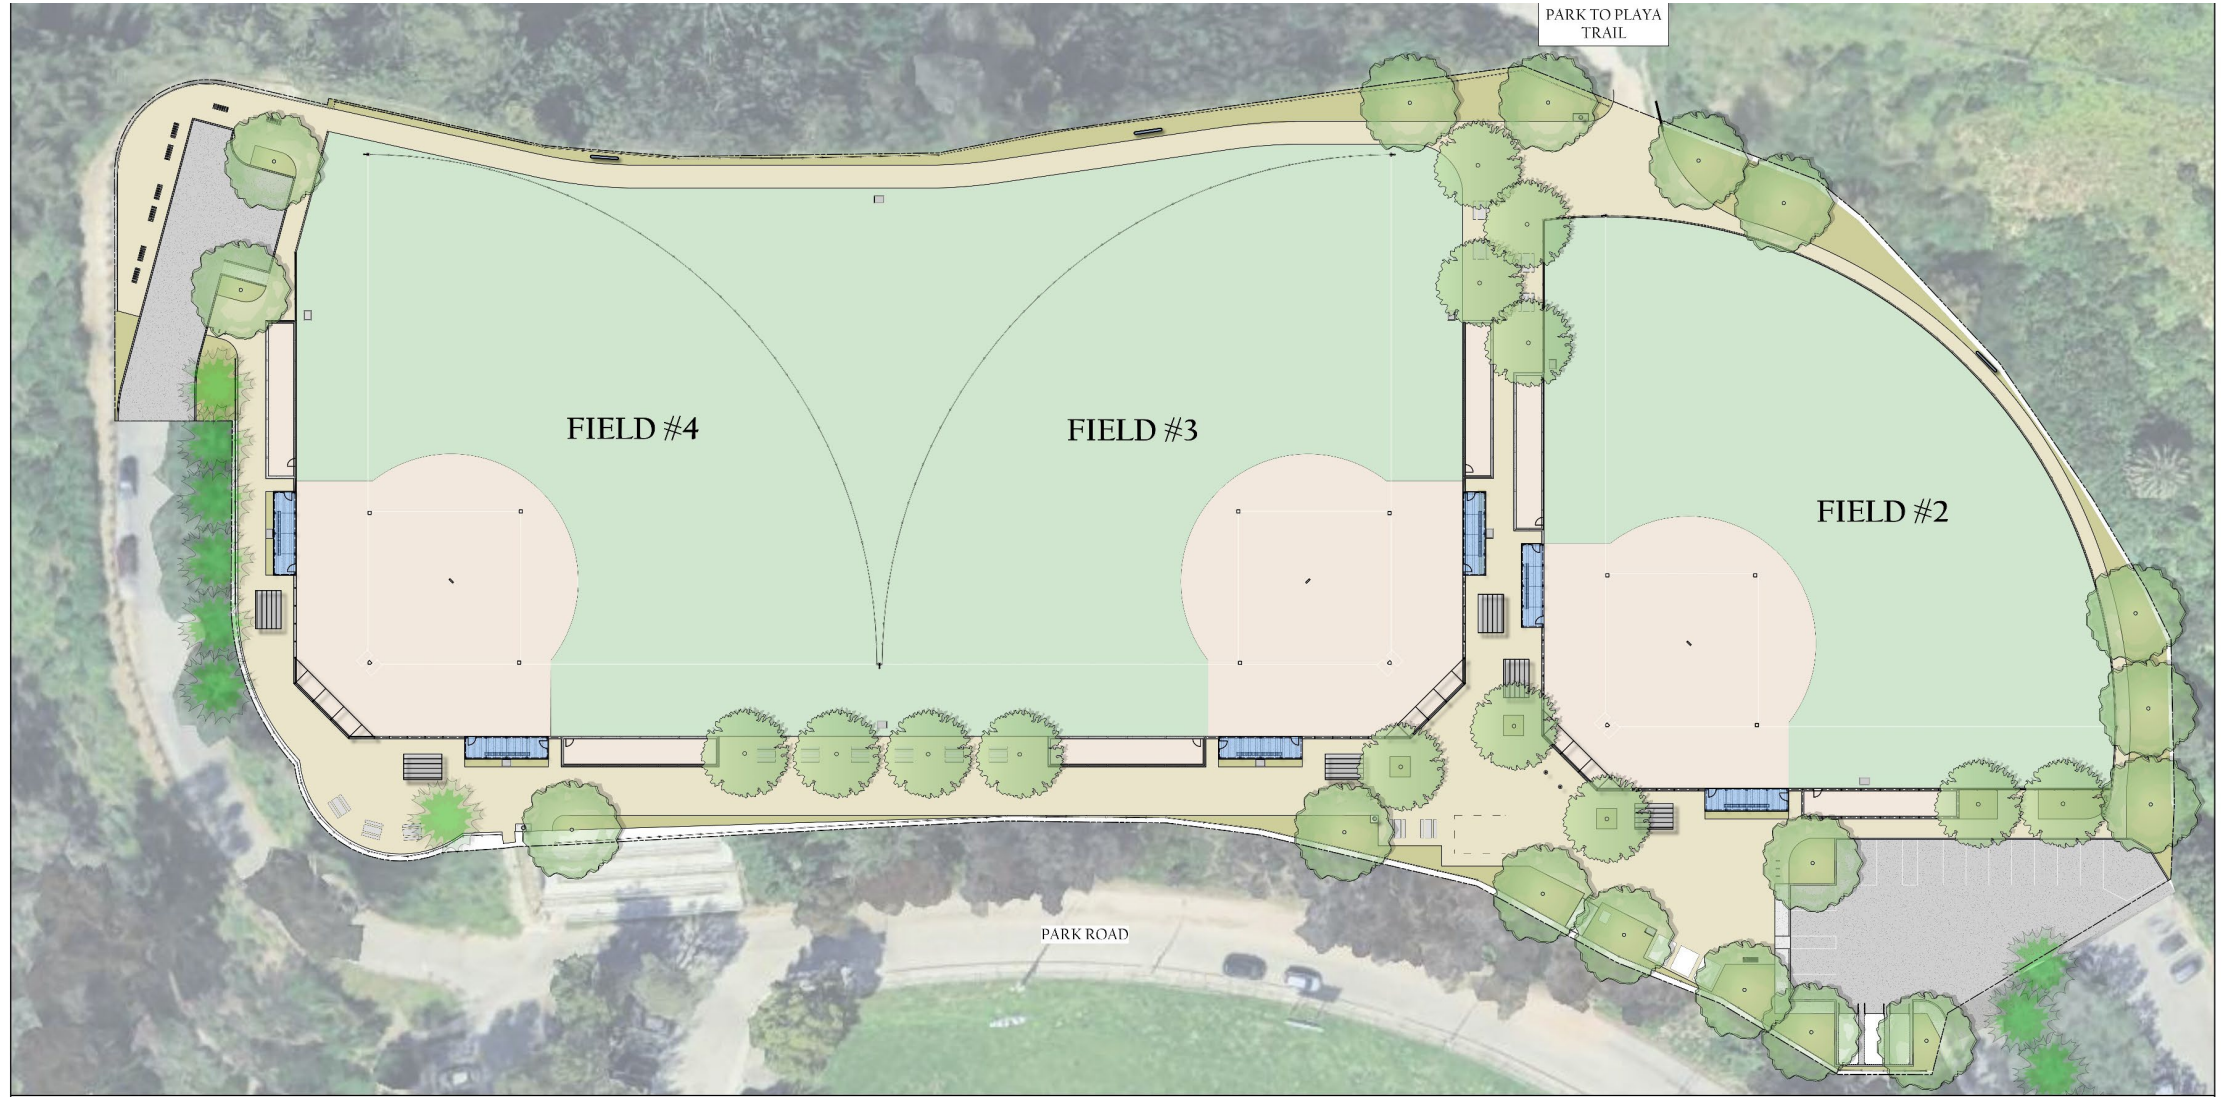

**PARK PLAN**  
Scale: 1:300



# Project Summary - Fields #2, #3, #4

This project will remove all existing equipment and utilize the soil stockpile to address continuous land settlement on all three fields.

Construction will include new grading and drainage, field equipment, walkways, seating areas and landscaping.

New restrooms will replace the current trailer.

The Field #2 parking lot will be regraded with new accessible parking.

The Field #4 parking lot will be modified to provide new overlook seating, fire access and accessible parking for special events.

## Fields #2, 3, 4





# Project Schedule - Fields #2, #3, #4

## August

Construction fencing and parking lot closures

Demolition of existing equipment

Construction drawings, engineering and plan check

## September & October

Infield removal & stockpile, Irrigation system modifications

Construction bidding, contract approvals

## October - January

Construction

## February 2027

Grand Opening



# Additional Projects at Culver City Park

## Slope Clearance

Clearance of brush from the drainage culverts in preparation of site surveys and for fire risk reduction.

This work is nearly complete.

## Trail Feasibility Study

Survey and explore potential conversion of drainage swales in trails. Fall 2026

## Tree Survey

Location and identification of park trees and invasive species. Funding pending grant application.

## Goats

Scheduled for mid-August

## Dog Park

Fence repairs, tree planting, signage. Fall 2026
